



ENGINEERING SUCCESS TOGETHER

WEEKLY SUMMARY REPORT

Client:	Needham DPW	Dates:	8/20/2016 to 8/26/2016
Contract:	Downtown Improvements		
Contractor:	MDR Construction Co., Inc.	Inspector on site:	DB/MH


WORK COMPLETED THIS WEEK

- Saw cutting of existing pavement for installation of new drainage
- Drain and manhole installation continued in front of Common to Highland Ave. intersection
- Delivery of additional catch basins
- Temporary trench pavement installation
- 2 hour work delay 8/23 due to SUV parked in no perking zone
- Cleanup and preparation for parade on Saturday
- Construction layout is continuing
- Shop drawings continue to be submitted and processed
- BETA, DPW, and MDR are continuously discussing construction logistics and schedules


WORK ANTICIPATED FOR NEXT WEEK

- Complete main drain installation in Highland Ave.
- Install catch basins and connecting drain pipe in multiple locations
- Install temporary pavement
- Receive delivery of various construction materials
- Continue shop drawing submissions and processing

PHOTOS

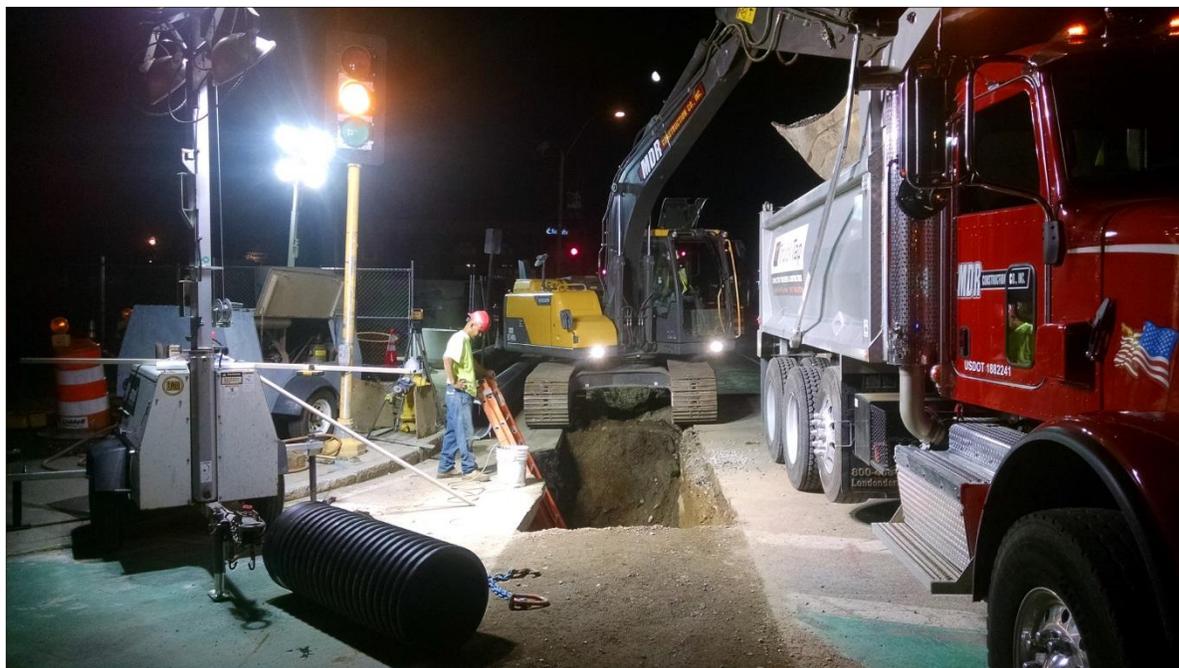

Drain Installation on Great plain Ave. east of Chapel St.
8/21/16

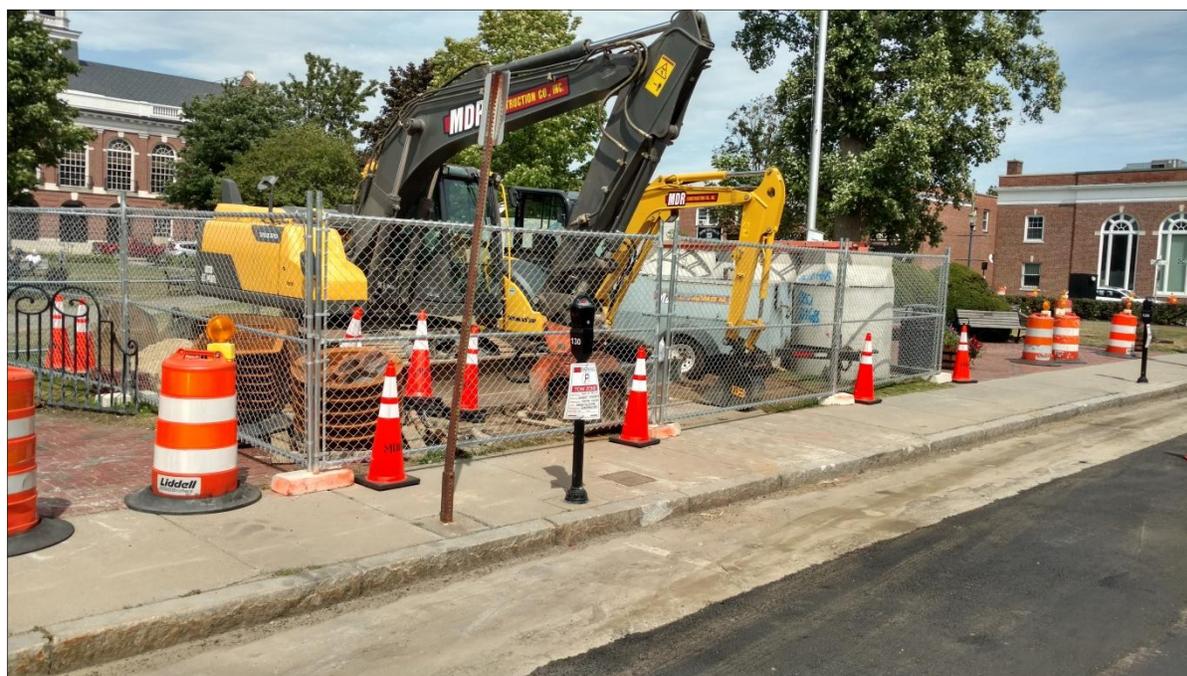


Contractor Staging Area on Town Common
8/25/16

PHOTOS



Completed Temporary Trench Paving
8/25/16

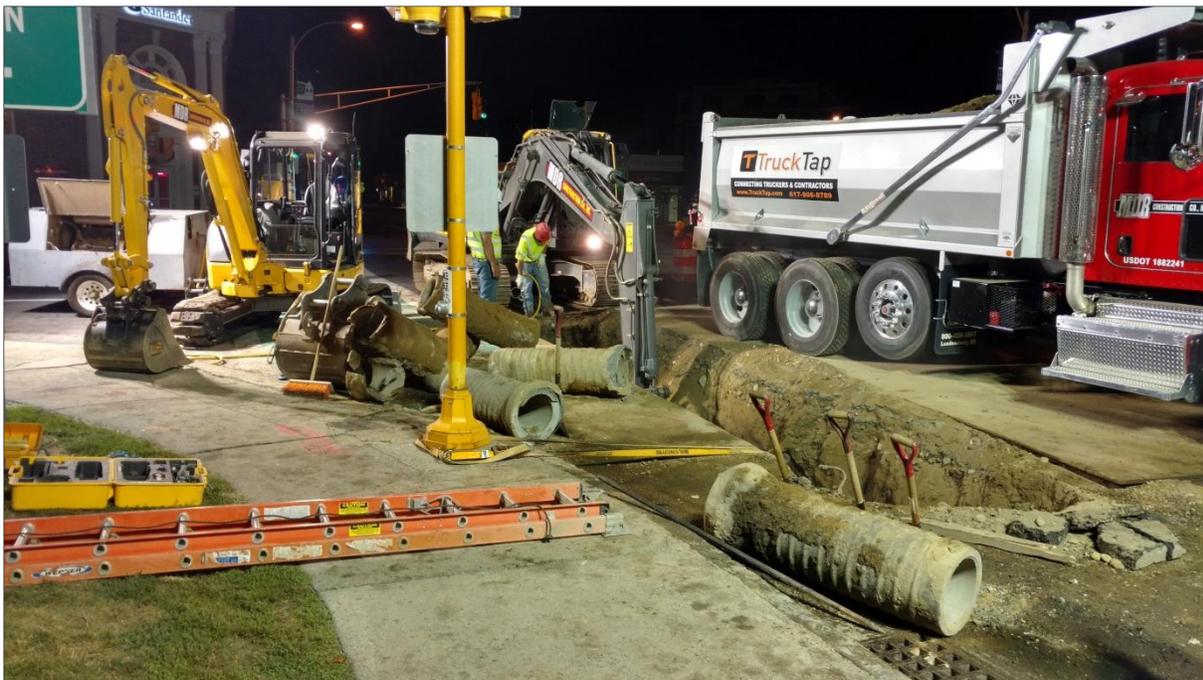

Existing Drain Removal and New Drain Installation at Intersection of Highland Ave. and Great Plain Ave.
8/25/16
