



ENGINEERING SUCCESS TOGETHER

WEEKLY SUMMARY REPORT

Clients: Newton & Needham DPW
Contract: Central Ave/Elliot St Bridge
Contractor: Aetna Bridge Company

Dates: 10/17/2016 to 10/21/2016
Inspector(s) on site: JD/ND

WORK COMPLETED THIS WEEK

- Install formwork and reinforcing for south sidewalk and north curb on bridge
- Pour concrete for south sidewalk and north curb on bridge
- Excavate for and install underground electrical vault on west bridge approach
- Install drainage structures and piping on east bridge approach
- Install underground utility conduit on west bridge approach

WORK ANTICIPATED FOR NEXT WEEK

- Install formwork for sidewalks on bridge approaches
- Install cemented stone masonry portion of northwest wingwall
- Excavate for and install underground electrical vaults on east bridge approach
- Install underground utility conduit on bridge approaches
- Install formwork for east abutment cap

CONSTRUCTION SCHEDULE STATUS

- Construction remains on schedule. The bridge is scheduled to re-open to vehicular traffic and to pedestrian traffic on the south sidewalk in mid-December. The contractor will return in the Spring of 2017 to complete the north sidewalk and punch list items.

PHOTOS



Formwork and Reinforcing for North Curb on Bridge
10/18/2016




Installing Reinforcing Steel for South Sidewalk on Bridge
10/18/2016

PHOTOS



Final Preparations for Pouring Concrete for South Sidewalk and North Curb
10/19/2016

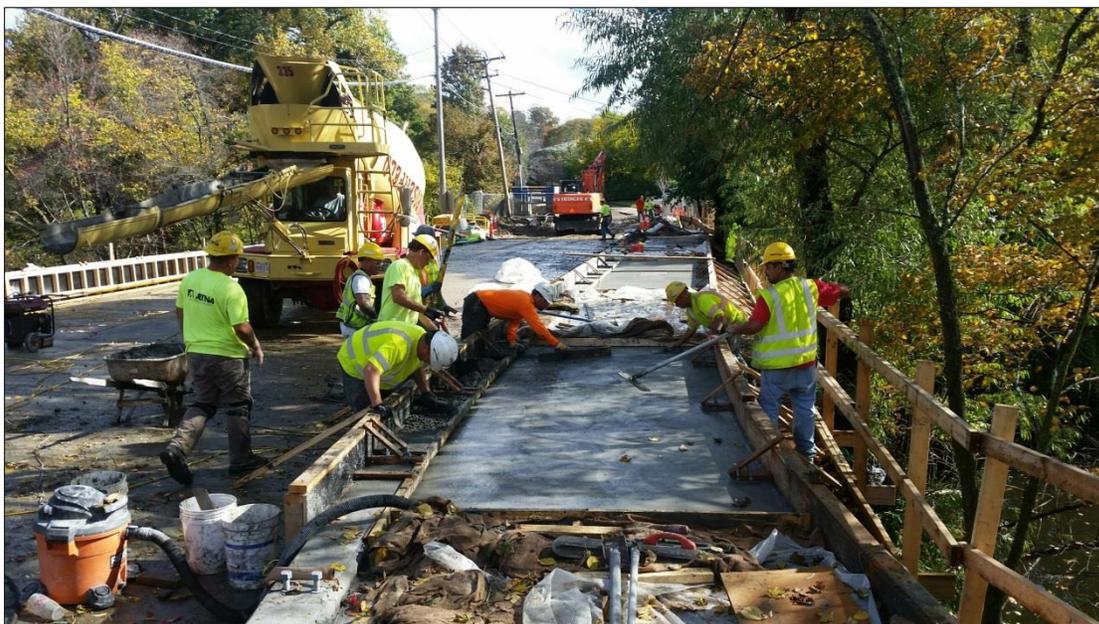

Pouring and Finishing Concrete for South Sidewalk on Bridge
10/21/2016
