

## **WEEKLY SUMMARY REPORT**

Client: Needham DPW Dates: 9/30/2016 to 10/7/2016

Contract: Downtown Improvements

Contractor: MDR Construction Co., Inc. Inspector on site: DB/ND

## WORK COMPLETED THIS WEEK

- Completed installation of all the drainage
- Temporary trench pavement was installed
- Completed installation of all the concrete mast arm and control cabinet foundations
- Saw cutting continued for the trench for the proposed electric and traffic signal conduit along with the proposed granite curb
- Installation of the traffic signal, lighting and bollard conduits has begun
- Shop drawings continue to be submitted and processed
- BETA, DPW, and MDR are continuously discussing construction logistics and schedules

## WORK ANTICIPATED FOR NEXT WEEK

- Continue installation of the traffic signal and electrical conduit and hand holes
- Install temporary pavement
- Continue installation of traffic signal equipment
- Begin installation of the pedestrian signal post foundations
- Receive delivery of various construction materials including electrical conduit, light and bollard foundations and hand holes/pull boxes
- Continue shop drawing submissions and processing

## **PHOTOS**




Excavating for mast arm and control cabinet foundations using a vactor truck



Preparing to install the reinforcing cage for the mast arm foundation on the corner of Great Plain Ave. and Chapel Street



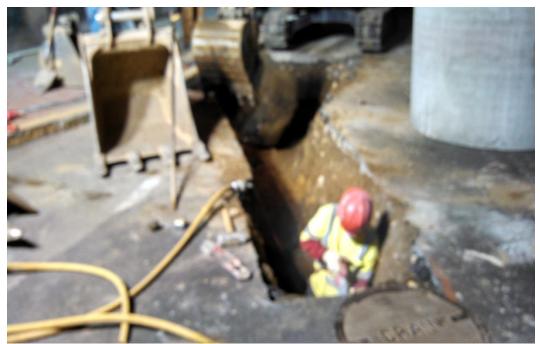

Installing drain lateral piping at station 10+68 in Great Plain Ave.

