



ENGINEERING SUCCESS TOGETHER

## WEEKLY SUMMARY REPORT

---

Client:	Needham DPW	Dates:	7/30/2016 to 8/5/2016
Contract:	Downtown Improvements	Inspector on site:	ND
Contractor:	MDR Construction Co., Inc.		

---

### WORK COMPLETED THIS WEEK

---

- Construction warning signage was installed in all approaching streets
- All trees designated for removal were taken down
- Temporary fencing was installed for a small “lay down” area on the west side of the common and behind the Town property at 66/68 Chestnut Street (Kerivan Lane property)
- Dig safe mark outs were completed
- Construction layout continued including layout for new drain facility locations
- Shop drawings continue to be submitted and processed
- BETA, DPW, and MDR are continuously discussing construction logistics and schedules

### WORK ANTICIPATED FOR NEXT WEEK

---

- Saw cutting of drainage trenches
- Multiple test pits will be excavated to determine various existing utility pipe/conduit elevations
- Install temporary office trailer behind the Town property at 66/68 Chestnut Street (Kerivan Lane property)
- Receive delivery of drainage components including pipe, manholes and catch basins
- Continue shop drawing submissions and processing

PHOTOS

---



Temporary fencing for lay down area on Common  
8/3/16



Temporary fencing for lay down area behind 66/68 Chestnut Street  
8/3/16

**PHOTOS**

---



Message board and warning sign at east end of project on Great Plain Ave.  
8/1/16




Removing branches of tree on common from bucket truck  
8/1/16

**PHOTOS**

---



Feeding branches of tree from common into chipper  
8/1/16

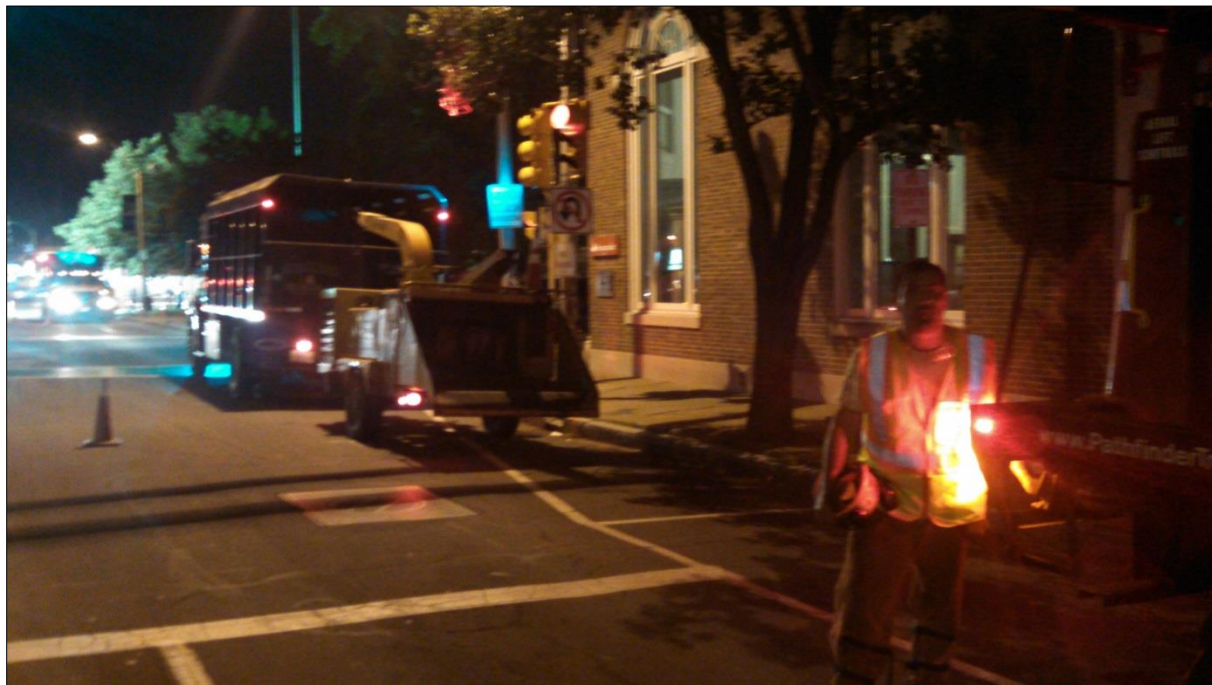

Removing trees on corner of Great Plain Ave and Highland Ave  
8/1/16
