



ENGINEERING SUCCESS TOGETHER

WEEKLY SUMMARY REPORT

Clients: Needham DPW
Contract: Rosemary Lake Dredging
Contractor: Maverick Construction Co., Inc.

Dates: 8/19/2019 to 8/23/2019
Inspector(s) on site:

WORK COMPLETED THIS WEEK

- Erosion control submittal provided by Maverick on Monday August 19th. BETA reviewed erosion control plan and requested resubmittal. Maverick provided resubmittal on Wednesday August 21st. Needham ConCom gave final approval Friday August 23rd. Information on erosion controls will be provided in later summary reports.
- Conducted turbidity and flow monitoring along Rosemary Brook on Friday morning.

WORK ANTICIPATED FOR NEXT WEEK

- Maverick to install erosion controls. Needham Conservation Commission to inspect prior to Wednesday (8/28) meeting with MassDEP.
- On-site pre-construction meeting with Jill Provencal of MassDEP scheduled for August 28th at 10am to inspect the erosion controls.
- Weekly turbidity monitoring to be conducted along Rosemary Brook.


PHOTOS



Station 5.5 (Whalen) – Additional sediment building near fallen tree at station 5.5 on Whalen property. (8/23/2019)



Station 5.2 (Whalen) – Sediment building along bank at Station 5.2 on Whalen property. (8/23/2019)

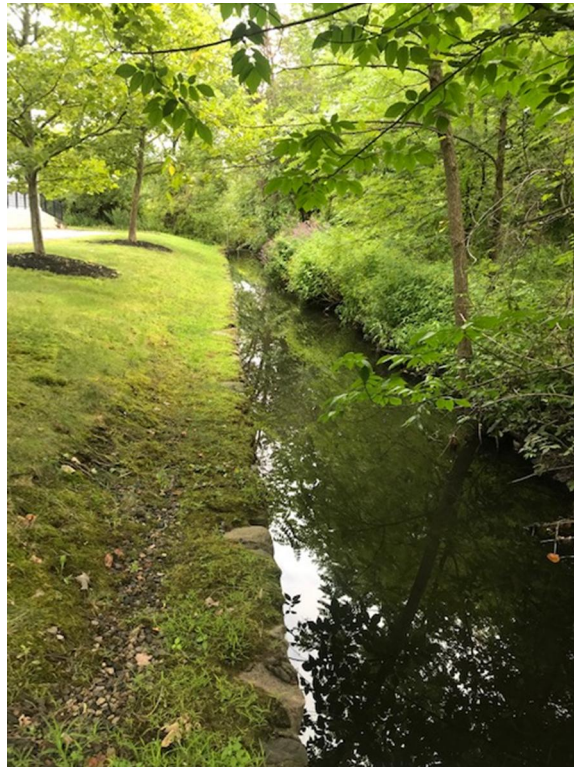

Station 2 (West Street) – Station 2 remains in similar conditions to previous monitoring rounds.
(8/23/2019)



Station 1 (Petrini Apartments) – Station 1 appeared similar to previous week's visit. Flow of brook at higher velocity than previous monitoring; however, it was noted that it had rained the night before monitoring. (8/23/2019)
